

PROFILE EDGE FINISHES

The edges of a shape can be left as a raw cut, folded back over to create a finished edge, or left as the factory edge of the sheet. **The factory edge can be used on both edges of the shape ONLY if the total length of the sides equals 48".*

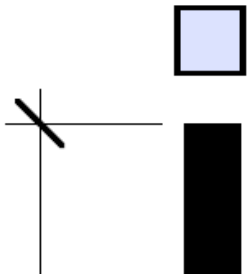

Click the check box at the end of the shape to indicate that a finished edge is required.

Click the "Factory Edge" check box at the bottom of the profile sheet to indicate that a factory edge is required.

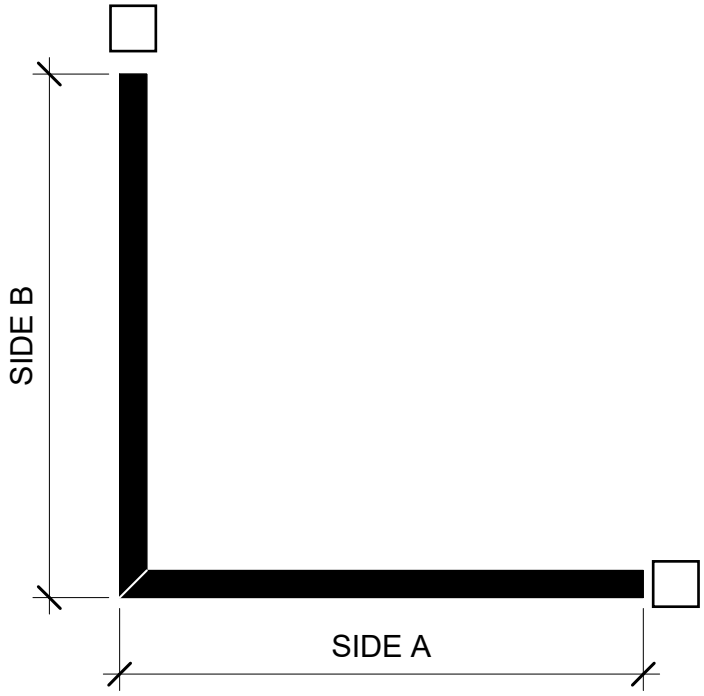

SUGGESTED USES:
2-SIDED
FURRDOWNS
CEILING CLOUD
PERIMETERS
LIGHT COVES
CORNER COLUMN
WRAPS

QUANTITY			PCS
LENGTH (12'-0" MAX)			
BOARD THICKNESS			5/8"
SIDE A	FACTORY EDGE	☐	
SIDE B	FACTORY EDGE	☐	

*FACTORY EDGE AVAILABLE ONLY ON ONE SIDE
UNLESS TOTAL OF SIDE A AND SIDE B EQUALS 48"

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	90 DEG CORNER	
	Project number	QS-001
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"




SUGGESTED USES:
BULKHEAD
FURRDOWNS
COLUMN WRAPS

QUANTITY			PCS
LENGTH (12'-0" MAX)			
BOARD THICKNESS			
SIDE A			
SIDE B	FACTORY EDGE	☐	
SIDE C	FACTORY EDGE	☐	

*FACTORY EDGE AVAILABLE ONLY ON ONE SIDE UNLESS TOTAL OF SIDES A, B AND C EQUALS 48"

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	U-SHAPE	
	Project number	QS-004
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"

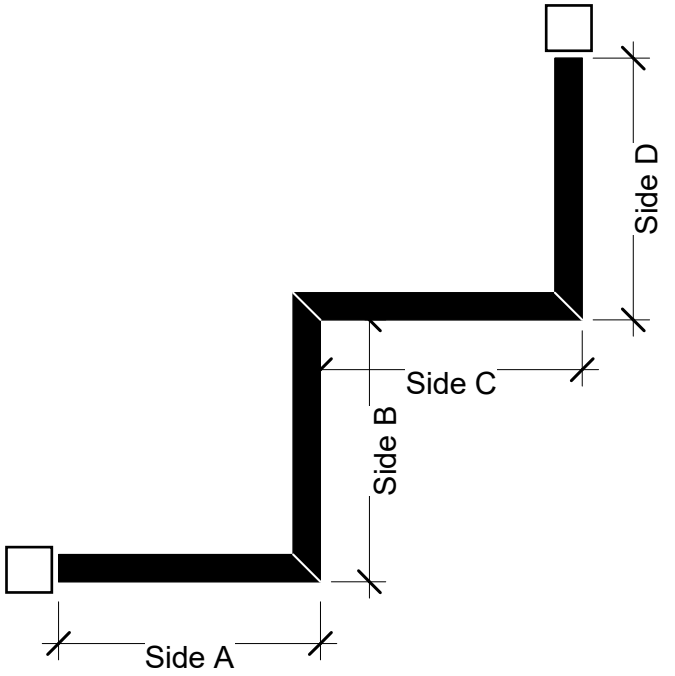


SUGGESTED USES:
FURRDOWNS
CORNICE

QUANTITY			PCS
LENGTH (12'-0" MAX)			
BOARD THICKNESS			
SIDE A	FACTORY EDGE	☐	
SIDE B			
SIDE C			
SIDE D	FACTORY EDGE	☐	

*FACTORY EDGE AVAILABLE ONLY ON ONE SIDE
UNLESS TOTAL OF SIDES A, B, C AND D EQUALS 48"

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	W-SHAPE	
	Project number	QS-005
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"

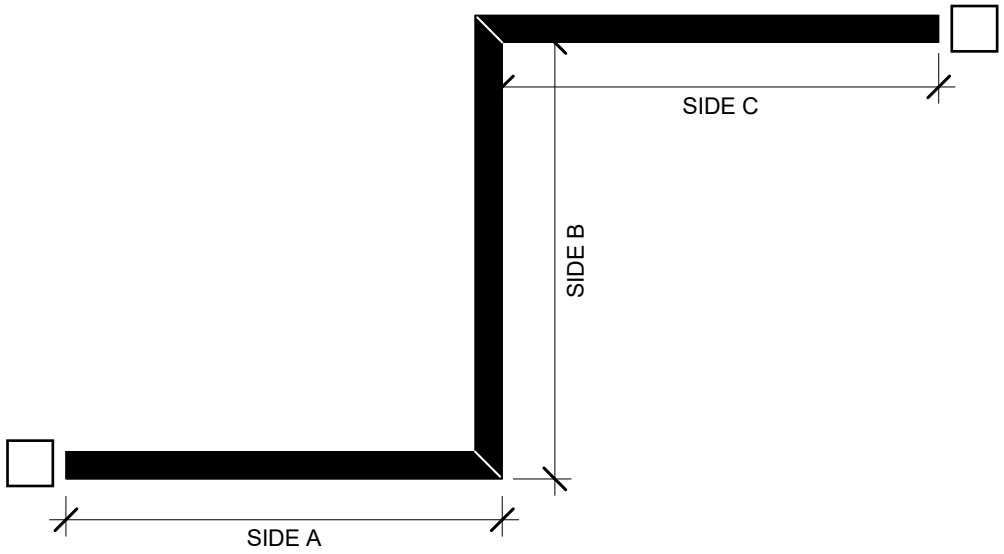

SUGGESTED USES:
FURRDOWNS
CEILING
TRANSITIONS
CORNICE

QUANTITY		PCS
LENGTH (12'-0" MAX)		
BOARD THICKNESS		
SIDE A	FACTORY EDGE ☐	
SIDE B		
SIDE C	FACTORY EDGE ☐	


*FACTORY EDGE AVAILABLE ONLY ON ONE SIDE
UNLESS TOTAL OF SIDES A, B, C AND D EQUALS 48"

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT Z-SHAPE

Project number	QS-006
Date	
Requested by	
Delivery Date	Scale 3" = 1'-0"

1/14/2018 4:45:24 PM

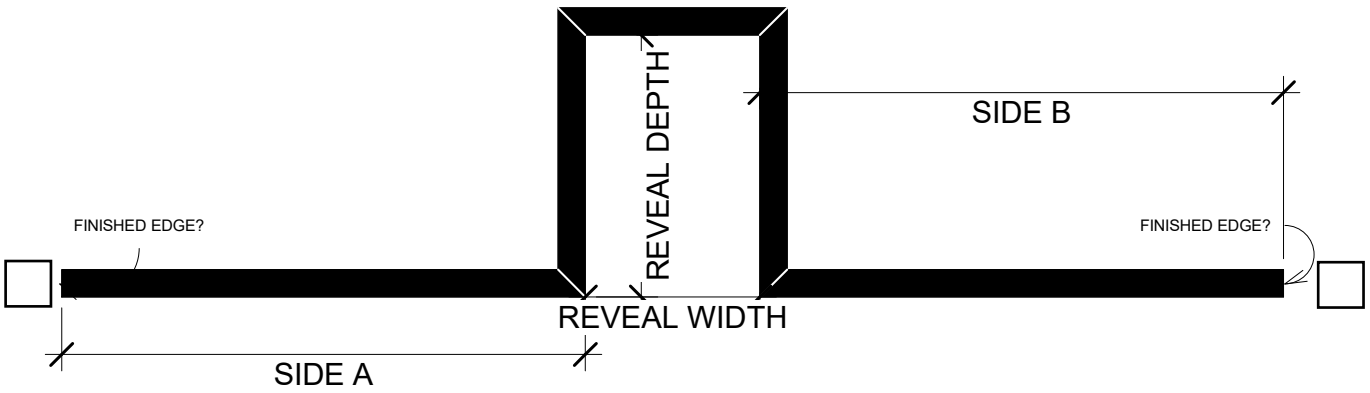


SUGGESTED USES:
WALL AND CEILING
REVEALS
LINEAR LIGHT
POCKETS

QUANTITY			PCS
LENGTH (12'-0" MAX)			
BOARD THICKNESS			
SIDE A	FACTORY EDGE	☐	
SIDE B	FACTORY EDGE	☐	
REVEAL WIDTH			
REVEAL DEPTH			

*FACTORY EDGE AVAILABLE ONLY ON ONE SIDE
UNLESS TOTAL OF SIDE A AND SIDE B EQUALS 48"

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	REVEAL	
	Project number	QS-007
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"




SUGGESTED USES:
WALL AND CEILING
REVEALS
LINEAR LIGHT
WINDOW RETURNS

QUANTITY			PCS
LENGTH (12'-0" MAX)			
BOARD THICKNESS			
SIDE A	FACTORY EDGE	☐	

*FACTORY EDGE AVAILABLE ONLY ON ONE SIDE
UNLESS TOTAL OF SIDE A AND SIDE B EQUALS 48"

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	WINDOW RETURNS	
	Project number	QS-008
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"

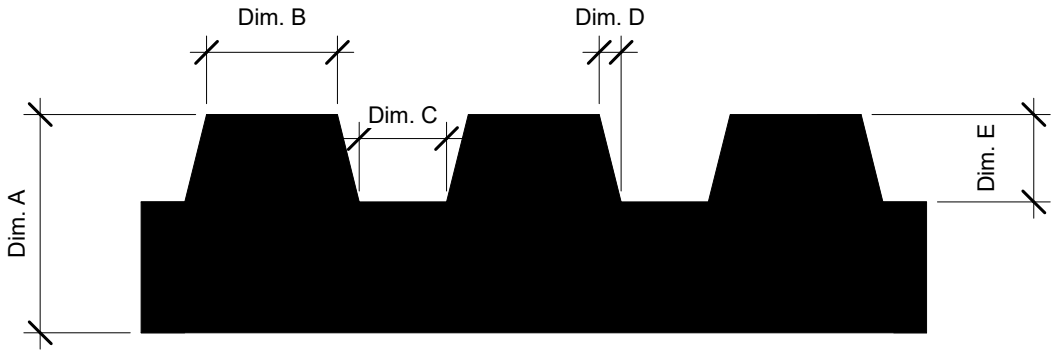


QUANTITY PCS	
LENGTH (12'-0" MAX)	
BOARD THICKNESS	
DIMENSION A	
DIMENSION B	
DIMENSION C	
DIMENSION D	
DIMENSION E	

SUGGESTED USES:
WALL TOPOUT AT FLUTED DECKS (PERPENDICULAR TO FLUTES)

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	CASTLE CUTS	
	Project number	QS-009
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"

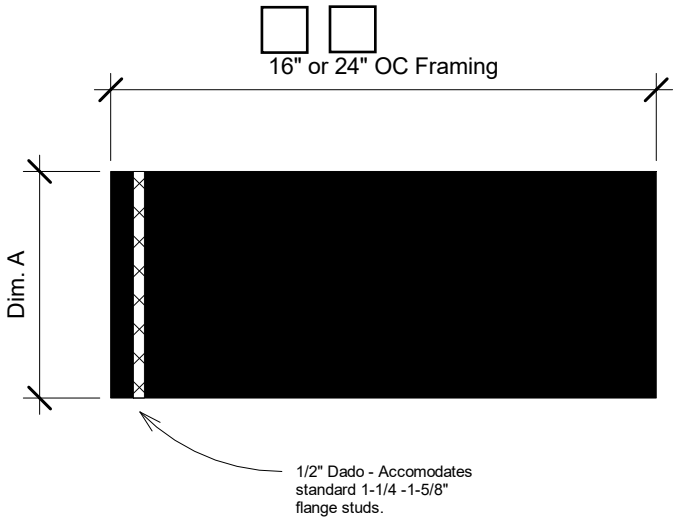

SUGGESTED USES:
BLOCKING FOR:
GRAB BARS
HANDRAILS
TV/DIGITAL SIGNAGE
ANY WALL HUNG EQUIPMENT

QUANTITY PCS	
BOARD TYPE	FSC PLYWOOD FIRE RATED
BOARD THICKNESS	3/4"
DIMENSION A	
SPACING 16" ☐ 24" ☐	OTHER

FSC CERTIFICATION REQUIRED NO

BLACKHAUS
BUILT WITHOUT COMPROMISE

PROJECT	PREFAB BLOCKING	
	Project number	QS-011
	Date	
	Requested by	
	Delivery Date	Scale 3" = 1'-0"
